2011' - 2014' FMS Painting Schedule

ID	Task Name	Start	Finish
1			
2	Butte Hall Common Areas	Mon 3/28/11	Mon 3/28/11
3	1st Floor	Mon 3/28/11	Fri 4/15/11
4	2nd Floor	Mon 4/18/11	Wed 4/27/11
5	3rd Floor	Thu 4/28/11	Mon 5/9/11
6	4th Floor	Tue 5/10/11	Thu 5/19/11
7	5th Floor	Fri 9/16/11	Tue 9/27/11
8	6th Flooor	Wed 9/28/11	Fri 10/7/11
9	7th Floor	Mon 10/10/11	Wed 10/19/11
10	Butte Office / Classrooms	Thu 5/19/11	Thu 5/19/11
11	1st Floor	Fri 5/20/11	Thu 6/2/11
12	2nd Floor	Fri 6/3/11	Thu 6/23/11
13	3rd Floor	Fri 7/8/11	Thu 7/21/11
14	4th Floor	Fri 7/22/11	Thu 8/11/11
15	5th Floor	Fri 8/12/11	Thu 8/25/11
16	6th Flooor	Fri 8/26/11	Thu 9/15/11
17	7th Floor	Thu 12/15/11	Wed 1/4/12
18			
19	SELV Exterior	Fri 6/24/11	Thu 7/7/11
20			
21	PHSC Common Areas	Thu 10/20/11	Thu 10/20/11
22	1st Floor	Thu 10/20/11	Wed 12/14/11
23	2nd Floor	Thu 2/2/12	Wed 3/28/12
24	3rd Floor	Thu 3/29/12	Wed 5/16/12
25	PHSC Office / Classrooms	Thu 1/5/12	Thu 1/5/12
26	1st Floor	Thu 1/5/12	Wed 1/18/12
27	2nd Floor	Thu 1/19/12	Wed 2/1/12
28	3rd Floor	Thu 5/17/12	Wed 5/23/12
29			
30	MODC Common Areas	Mon 8/27/12	Mon 8/27/12
31	1st Floor	Mon 8/27/12	Tue 10/2/12
32	2nd Floor	Wed 10/3/12	Thu 11/1/12
33	MODC Office / Classroom	Thu 5/24/12	Thu 5/24/12
34	1st Floor	Thu 5/24/12	Wed 6/6/12
35	2nd Floor	Thu 6/7/12	Fri 6/22/12
36			
37	MODC EXTERIOR	Mon 6/25/12	Fri 7/13/12
38			
39	MLIB Common Area	Fri 11/2/12	Fri 11/2/12
40	Basement	Fri 11/2/12	Thu 11/29/12
41	1st Floor	Fri 3/8/13	Thu 5/9/13
42	2nd Floor	Fri 5/10/13	Thu 6/13/13
43	3rd Floor	Fri 11/30/12	Thu 12/27/12
44	4th Floor	Fri 2/8/13	Thu 3/7/13
45	MLIB Office / Classroom	Mon 7/16/12	Mon 7/16/12
46	Basement	Mon 7/16/12	Fri 8/24/12
47	1st Floor	Fri 12/28/12	Thu 2/7/13
48	2nd Floor	Fri 6/14/13	Thu 7/4/13
49	3rd Floor	Fri 7/5/13	Mon 7/29/13
50	4th Floor	Tue 7/30/13	Wed 8/21/13
51			
52	PLMS Common Areas	Thu 8/22/13	Thu 8/22/13
53	Basement	Thu 8/22/13	Wed 9/11/13
54	1st Floor	Thu 9/12/13	Wed 11/20/13
55	2nd Floor	Thu 11/21/13	Wed 12/4/13
56	3rd Floor	Tue 2/4/14	Mon 3/10/14
57	PLMS Office / Classroom	Thu 12/5/13	Thu 12/5/13
58	Basement	Thu 12/5/13	Wed 12/18/13
59	1st Floor	Thu 12/19/13	Mon 1/6/14
60	2nd Floor	Tue 1/7/14	Mon 1/20/14
61	3rd Floor	Tue 1/21/14	Mon 2/3/14

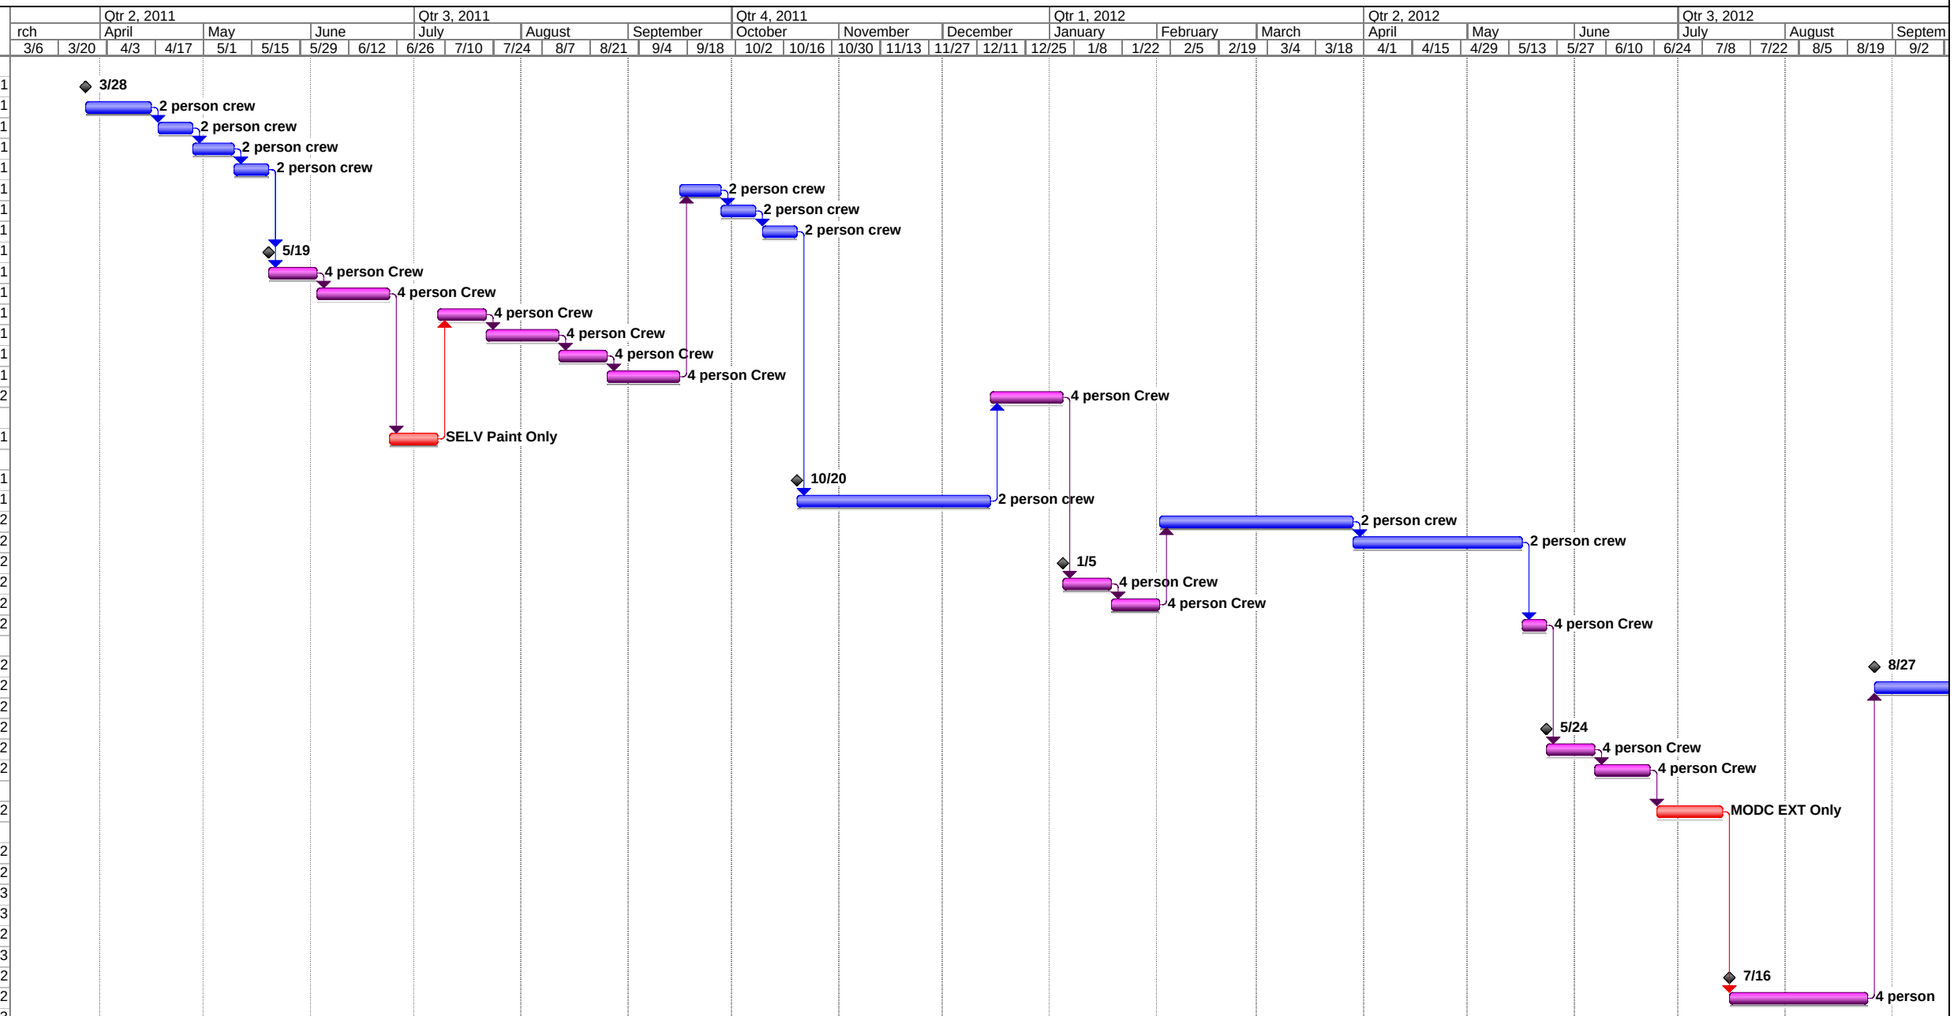

Project: Revised2011thru2014Painting
Date: Fri 2/18/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

By: Sean Greenwald 1

2011' - 2014' FMS Painting Schedule

ID	Task Name	Start	Finish
1			
2	Butte Hall Common Areas	Mon 3/28/11	Mon 3/28/11
3	1st Floor	Mon 3/28/11	Fri 4/15/11
4	2nd Floor	Mon 4/18/11	Wed 4/27/11
5	3rd Floor	Thu 4/28/11	Mon 5/9/11
6	4th Floor	Tue 5/10/11	Thu 5/19/11
7	5th Floor	Fri 9/16/11	Tue 9/27/11
8	6th Flooor	Wed 9/28/11	Fri 10/7/11
9	7th Floor	Mon 10/10/11	Wed 10/19/11
10	Butte Office / Classrooms	Thu 5/19/11	Thu 5/19/11
11	1st Floor	Fri 5/20/11	Thu 6/2/11
12	2nd Floor	Fri 6/3/11	Thu 6/23/11
13	3rd Floor	Fri 7/8/11	Thu 7/21/11
14	4th Floor	Fri 7/22/11	Thu 8/11/11
15	5th Floor	Fri 8/12/11	Thu 8/25/11
16	6th Flooor	Fri 8/26/11	Thu 9/15/11
17	7th Floor	Thu 12/15/11	Wed 1/4/12
18			
19	SELV Exterior	Fri 6/24/11	Thu 7/7/11
20			
21	PHSC Common Areas	Thu 10/20/11	Thu 10/20/11
22	1st Floor	Thu 10/20/11	Wed 12/14/11
23	2nd Floor	Thu 2/2/12	Wed 3/28/12
24	3rd Floor	Thu 3/29/12	Wed 5/16/12
25	PHSC Office / Classrooms	Thu 1/5/12	Thu 1/5/12
26	1st Floor	Thu 1/5/12	Wed 1/18/12
27	2nd Floor	Thu 1/19/12	Wed 2/1/12
28	3rd Floor	Thu 5/17/12	Wed 5/23/12
29			
30	MODC Common Areas	Mon 8/27/12	Mon 8/27/12
31	1st Floor	Mon 8/27/12	Tue 10/2/12
32	2nd Floor	Wed 10/3/12	Thu 11/1/12
33	MODC Office / Classroom	Thu 5/24/12	Thu 5/24/12
34	1st Floor	Thu 5/24/12	Wed 6/6/12
35	2nd Floor	Thu 6/7/12	Fri 6/22/12
36			
37	MODC EXTERIOR	Mon 6/25/12	Fri 7/13/12
38			
39	MLIB Common Area	Fri 11/2/12	Fri 11/2/12
40	Basement	Fri 11/2/12	Thu 11/29/12
41	1st Floor	Fri 3/8/13	Thu 5/9/13
42	2nd Floor	Fri 5/10/13	Thu 6/13/13
43	3rd Floor	Fri 11/30/12	Thu 12/27/12
44	4th Floor	Fri 2/8/13	Thu 3/7/13
45	MLIB Office / Classroom	Mon 7/16/12	Mon 7/16/12
46	Basement	Mon 7/16/12	Fri 8/24/12
47	1st Floor	Fri 12/28/12	Thu 2/7/13
48	2nd Floor	Fri 6/14/13	Thu 7/4/13
49	3rd Floor	Fri 7/5/13	Mon 7/29/13
50	4th Floor	Tue 7/30/13	Wed 8/21/13
51			
52	PLMS Common Areas	Thu 8/22/13	Thu 8/22/13
53	Basement	Thu 8/22/13	Wed 9/11/13
54	1st Floor	Thu 9/12/13	Wed 11/20/13
55	2nd Floor	Thu 11/21/13	Wed 12/4/13
56	3rd Floor	Tue 2/4/14	Mon 3/10/14
57	PLMS Office / Classroom	Thu 12/5/13	Thu 12/5/13
58	Basement	Thu 12/5/13	Wed 12/18/13
59	1st Floor	Thu 12/19/13	Mon 1/6/14
60	2nd Floor	Tue 1/7/14	Mon 1/20/14
61	3rd Floor	Tue 1/21/14	Mon 2/3/14

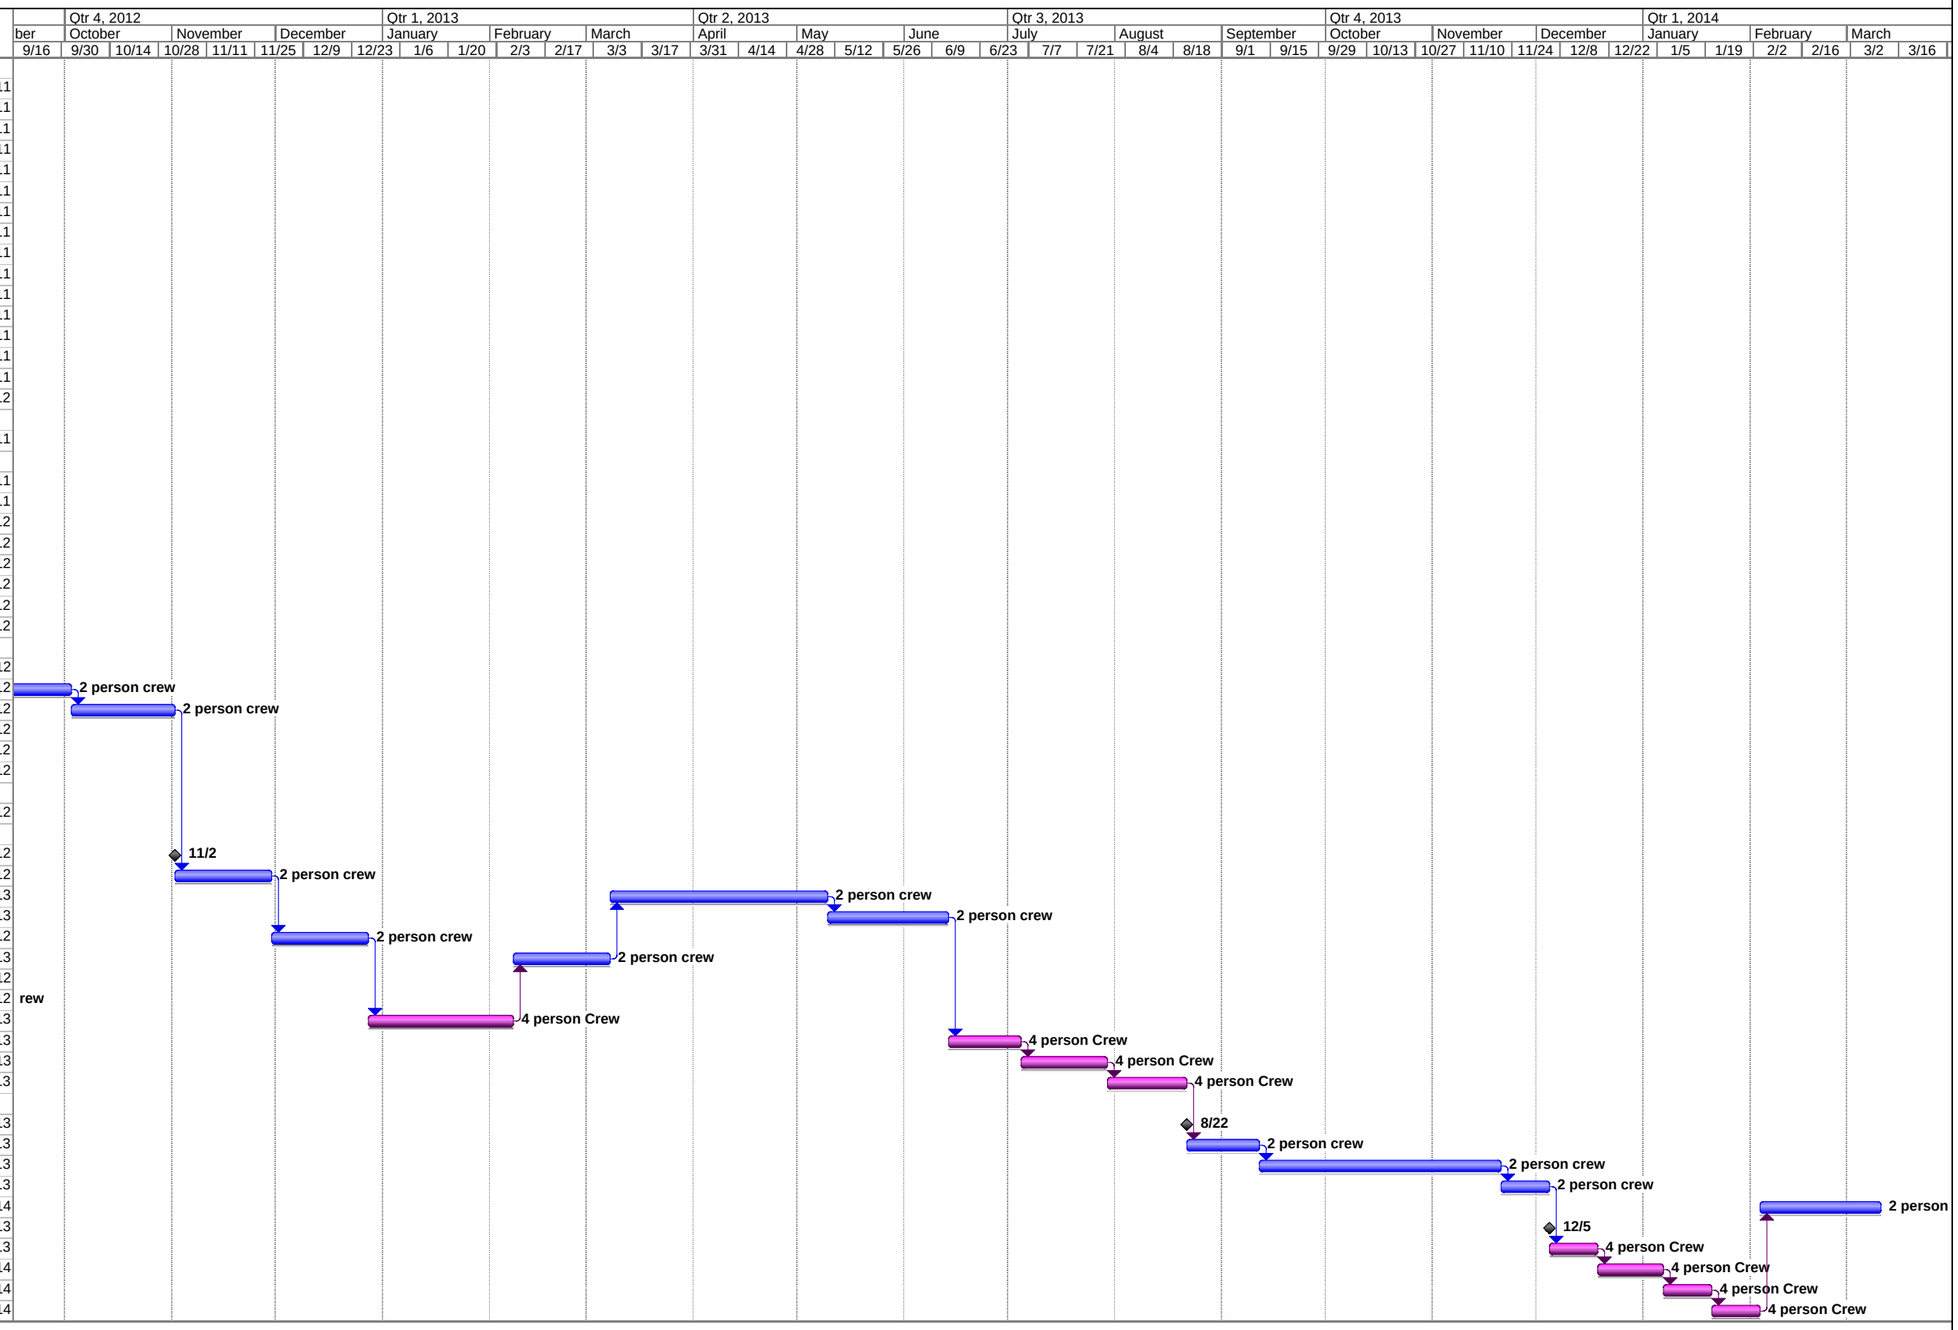

Project: Revised2011thru2014Painting
Date: Fri 2/18/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

By: Sean Greenwald 2
