ID	Task Mode	Task Name	Duration	Start	Finish
1		**CONCEPTUAL PROJECT TIMELINE - DESIGN PHASE**	**285 days**	**Fri 3/1/19**	**Thu 4/2/20**
2		**1 - Feasibility / Constructability**	**30 days**	**Fri 3/1/19**	**Thu 4/11/19**
3		Project Triage - Assign to Project Manager	14 days	Fri 3/1/19	Wed 3/20/19
4		Scope / Programming meeting with Requestor	1 day	Thu 3/21/19	Thu 3/21/19
5		Verify Availability of space / Construction Timeline	1 day	Fri 3/22/19	Fri 3/22/19
6		Verify Existing Conditions / Field Investigations	5 days	Mon 3/25/19	Fri 3/29/19
7		Verify Underground Utilities	2 days	Mon 4/1/19	Tue 4/2/19
8		Determine Impacts to Structural Components	2 days	Wed 4/3/19	Thu 4/4/19
9		Determine Points of Connection to Existing Utilities	2 days	Fri 4/5/19	Mon 4/8/19
10		Check Facility Condition Assessment for building needs	1 day	Tue 4/9/19	Tue 4/9/19
11		Determine Environmental or Cultural Impacts	1 day	Wed 4/10/19	Wed 4/10/19
12		Determine special testing and inspection needs	1 day	Thu 4/11/19	Thu 4/11/19
13		**2 - Programming / Budget / Schedule**	**30 days**	**Fri 4/12/19**	**Thu 5/23/19**
14		Conceptual Scope Development	7 days	Fri 4/12/19	Mon 4/22/19
15		Prepare Schematic Drawings	10 days	Tue 4/23/19	Mon 5/6/19
16		Determine Method of Constr / Contract or In-House	14 days	Tue 4/23/19	Fri 5/10/19
17		Determine Permitting Requirements	1 day	Tue 5/7/19	Tue 5/7/19
18		Review Hazardous Materials & Conditions	2 days	Wed 5/8/19	Thu 5/9/19
19		Determine CEQA Impacts / Mechoopda Tribe	1 day	Fri 5/10/19	Fri 5/10/19
20		Determine SWPPP / MS4 Storm Water Mgt Impacts	1 day	Mon 5/13/19	Mon 5/13/19
21		Prepare Programming Document / Conceptual Budget	7 days	Tue 5/14/19	Wed 5/22/19
22		Prepare Preliminary Schedule	1 day	Thu 5/23/19	Thu 5/23/19
23		**3 - Requestor Approval and Funding**	**60 days**	**Fri 5/24/19**	**Thu 8/15/19**
24		Requestor approval to proceed with Design	30 days	Fri 5/24/19	Thu 7/4/19
25		Approval by Requestor's Admin approving body	15 days	Fri 7/5/19	Thu 7/25/19
26		Funding Approval (PEWAF)	15 days	Fri 7/26/19	Thu 8/15/19
27		**4 - Procure Design Consultants / Gather Design Informatic**	**30 days**	**Fri 8/16/19**	**Thu 9/26/19**
28		Architect	30 days	Fri 8/16/19	Thu 9/26/19
29		Electrical Engineer	30 days	Fri 8/16/19	Thu 9/26/19
30		Mechanical Engineer	30 days	Fri 8/16/19	Thu 9/26/19
31		Structural Engineer	30 days	Fri 8/16/19	Thu 9/26/19
32		Civil Engineer	30 days	Fri 8/16/19	Thu 9/26/19
33		Fire Alarm (Johnson Controls)	30 days	Fri 8/16/19	Thu 9/26/19
34		Fire Sprinklers (Foothill)	30 days	Fri 8/16/19	Thu 9/26/19
35		Hazmat Survey / Abatement Specifications (Entek)	30 days	Fri 8/16/19	Thu 9/26/19
36		Obtain Requestor's Preferences / Furniture Layouts	30 days	Fri 8/16/19	Thu 9/26/19
37		CSUC FMS Trades	30 days	Fri 8/16/19	Thu 9/26/19
38		CSUC Computing & Communications Services (CCSV)	30 days	Fri 8/16/19	Thu 9/26/19
39		CSUC Telecommunications Services (TSRV)	30 days	Fri 8/16/19	Thu 9/26/19
40		CSUC Creative Media and Technology (CMT)	30 days	Fri 8/16/19	Thu 9/26/19
41		CSUC Environmental Health & Safety (EHS)	30 days	Fri 8/16/19	Thu 9/26/19
42		CSUC University Police (UPD)	30 days	Fri 8/16/19	Thu 9/26/19
43		CSUC Transportation Committee	30 days	Fri 8/16/19	Thu 9/26/19
44		CSUC Arboretum Committee	30 days	Fri 8/16/19	Thu 9/26/19
45		Air Quality Management District (AQMD)	30 days	Fri 8/16/19	Thu 9/26/19
46		**5 - Construction Document Development**	**45 days**	**Fri 9/27/19**	**Thu 11/28/19**
47		Specifications Development / Campus Standards	1 wk	Fri 9/27/19	Thu 10/3/19
48		50% Construction Document Development	3 wks	Fri 9/27/19	Thu 10/17/19
49		50% Construction Document Review	1 wk	Fri 10/18/19	Thu 10/24/19
50		Procure Consultants for plan review	4 wks	Fri 10/25/19	Thu 11/21/19
51		95% Construction Document Development	3 wks	Fri 10/25/19	Thu 11/14/19
52		95% Construction Document Review	1 wk	Fri 11/15/19	Thu 11/21/19
53		100% CD ready for plan review / A&E Stamped Plans	1 wk	Fri 11/22/19	Thu 11/28/19
54		**6 - Plan Review & Approval**	**90 days**	**Fri 11/29/19**	**Thu 4/2/20**
55		Code Compliance (Willdan)	3 wks	Fri 11/29/19	Thu 12/19/19
56		State Fire Marshal (SFM) - Fire and Life Safety	12 wks	Fri 11/29/19	Thu 2/20/20
57		Div. of the State Architect (DSA) - Access Compliance	12 wks	Fri 11/29/19	Thu 2/20/20
58		Certified Access Specialist (CASp) - Access Compliance	2 wks	Fri 11/29/19	Thu 12/12/19
59		CSU Seismic Peer Review	2 wks	Fri 11/29/19	Thu 12/12/19
60		Make redline corrections	2 wks	Fri 2/21/20	Thu 3/5/20
61		Agency Back-Check and Approval	2 wks	Fri 3/6/20	Thu 3/19/20
62		CSUC Campus Building Official / Building Permit	2 wks	Fri 3/20/20	Thu 4/2/20
63		100% Final Construction Documents	0 days	Thu 4/2/20	Thu 4/2/20

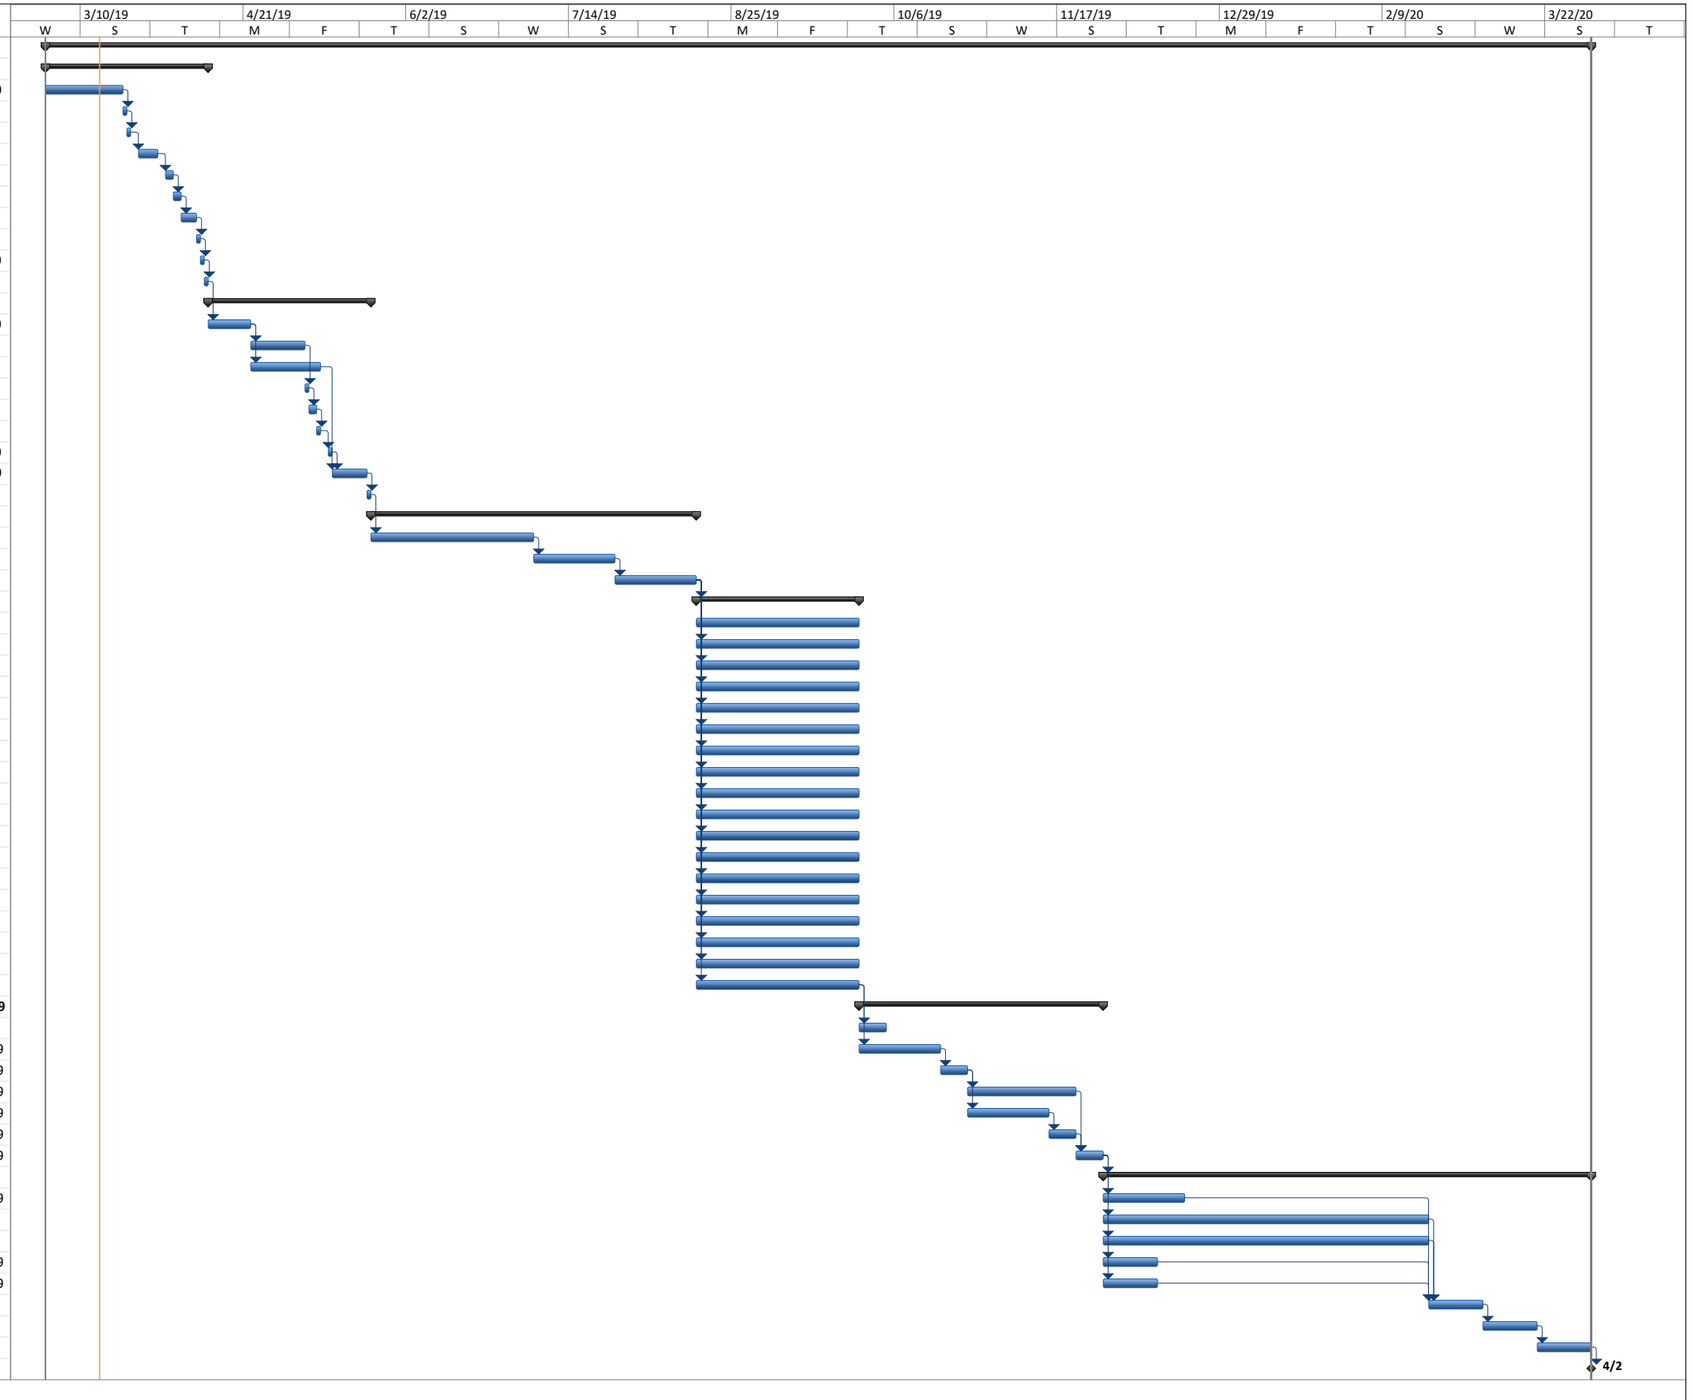

Project: Conceptual Project Timel
Date: Fri 3/15/19

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only		
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline		
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Progress		
